

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	**DEEPFAKE DETECTION OF AUDIO AND VIDEO**	**43 days?**	**Fri 30-10-26**	**Tue 29-12-26**		
2		1 day?	Fri 30-10-26	Fri 30-10-26		
3	**REQUIREMENT AND DESIGN**	**8 days**	**Fri 30-10-26**	**Tue 10-11-26**		**Project manager**
4	Project Planning and requirement analysis	2 days	Fri 30-10-26	Mon 02-11-26		Project manager
5	Define App features and Objectives	1 day	Tue 03-11-26	Tue 03-11-26	4	Project manager
6	Research Audio and Video Deepfake Detec	3 days	Wed 04-11-26	Fri 06-11-26	5	AI ML Developer
7	Select Dataset and AI model	2 days	Mon 09-11-26	Tue 10-11-26	6	AI ML Developer
8	Design UI and Application Workflow	2 days	Wed 04-11-26	Thu 05-11-26	5	UI UX Designer
9	**DATSET AND AI MODEL**	**16 days**	**Wed 11-11-26**	**Wed 02-12-26**		**AI ML Developer**
10	Collect Authentic and Fake Audio Dataset	4 days	Wed 11-11-26	Mon 16-11-26	7	Dataset Engineer
11	Collect Authentic and Fake vedio Dataset	4 days	Wed 11-11-26	Mon 16-11-26	7	Dataset Engineer
12	Preprocess and Validate Datasets	3 days	Tue 17-11-26	Thu 19-11-26	10,11	Dataset Engineer
13	Extract Audio Features and Video Frames	3 days	Fri 20-11-26	Tue 24-11-26	12	AI ML Developer
14	Train Audio Detection Model	4 days	Wed 25-11-26	Mon 30-11-26	13	AI ML Developer
15	Train video Detection Model	4 days	Wed 25-11-26	Mon 30-11-26	13	AI ML Developer
16	Evaluate and Optimize Both Models	2 days	Tue 01-12-26	Wed 02-12-26	14,15	AI ML Developer
17	**WEB APPLICATION DEVELOPMENT**	**25 days**	**Fri 06-11-26**	**Thu 10-12-26**		**WEB Developer**
18	Set Up Python and Streamlit Environment	1 day	Fri 06-11-26	Fri 06-11-26	8	PYTHON DEVELOPE
19	Develop App Home Page and Navigatio	2 days	Mon 09-11-26	Tue 10-11-26	18	UI UX Designer
20	Implement Audio and Video Upload	2 days	Wed 11-11-26	Thu 12-11-26	19	PYTHON DEVELOPE
21	Develop Audio Analysis Module	3 days	Fri 13-11-26	Tue 17-11-26	20	PYTHON DEVELOPE
22	Develop Video Analysis Module	3 days	Fri 13-11-26	Tue 17-11-26	20	PYTHON DEVELOPE
23	Integrate AI Models with Application	2 days	Thu 03-12-26	Fri 04-12-26	16,21,22	AI ML Developer
24	Create Results and Confidence Dashboard	2 days	Mon 07-12-26	Tue 08-12-26	23	WEB Developer
25	Add File Validation and Error Handling	2 days	Wed 09-12-26	Thu 10-12-26	24	Testing Engineer
26	**TESTING AND FINAL DELIVERY**	**13 days**	**Fri 11-12-26**	**Tue 29-12-26**		**Testing Engineer**
27	Test App with Sample Audio and Videos	3 days	Fri 11-12-26	Tue 15-12-26	25,24	Testing Engineer
28	Measure Model Performance and Accuracy	2 days	Wed 16-12-26	Thu 17-12-26	27	Testing Engineer
29	Improve UI and Fix Identified Bugs	3 days	Fri 18-12-26	Tue 22-12-26	28	WEB Developer
30	Deploy and Demonstrate the Applicatio	2 days	Wed 23-12-26	Thu 24-12-26	29	Deploy Engineer
31	Prepare Final Report and Presentation	2 days	Fri 25-12-26	Mon 28-12-26	30	ocumentation Manage
32	Final Review and Project Submission	1 day	Tue 29-12-26	Tue 29-12-26	31	Project manager

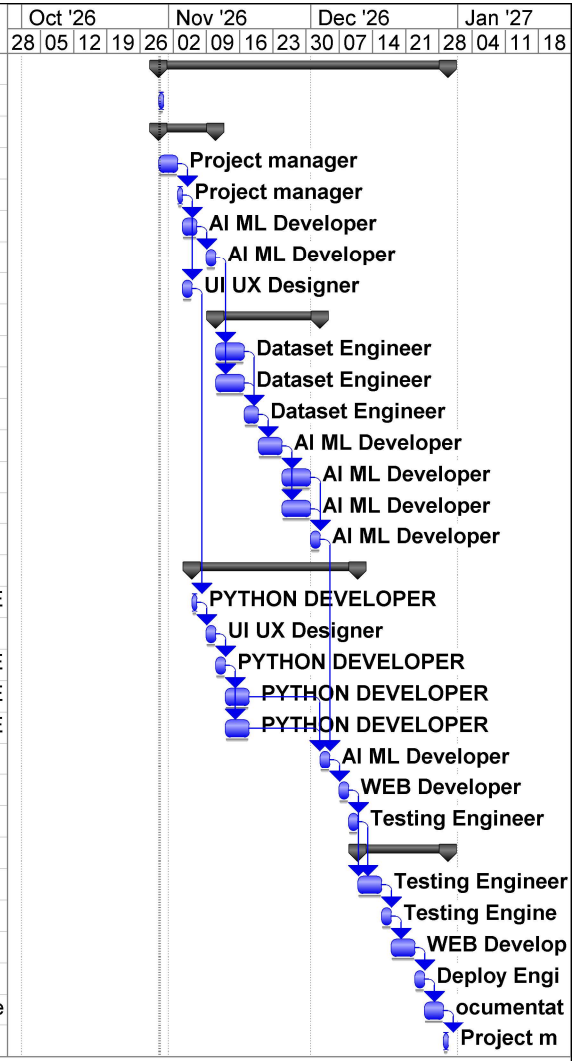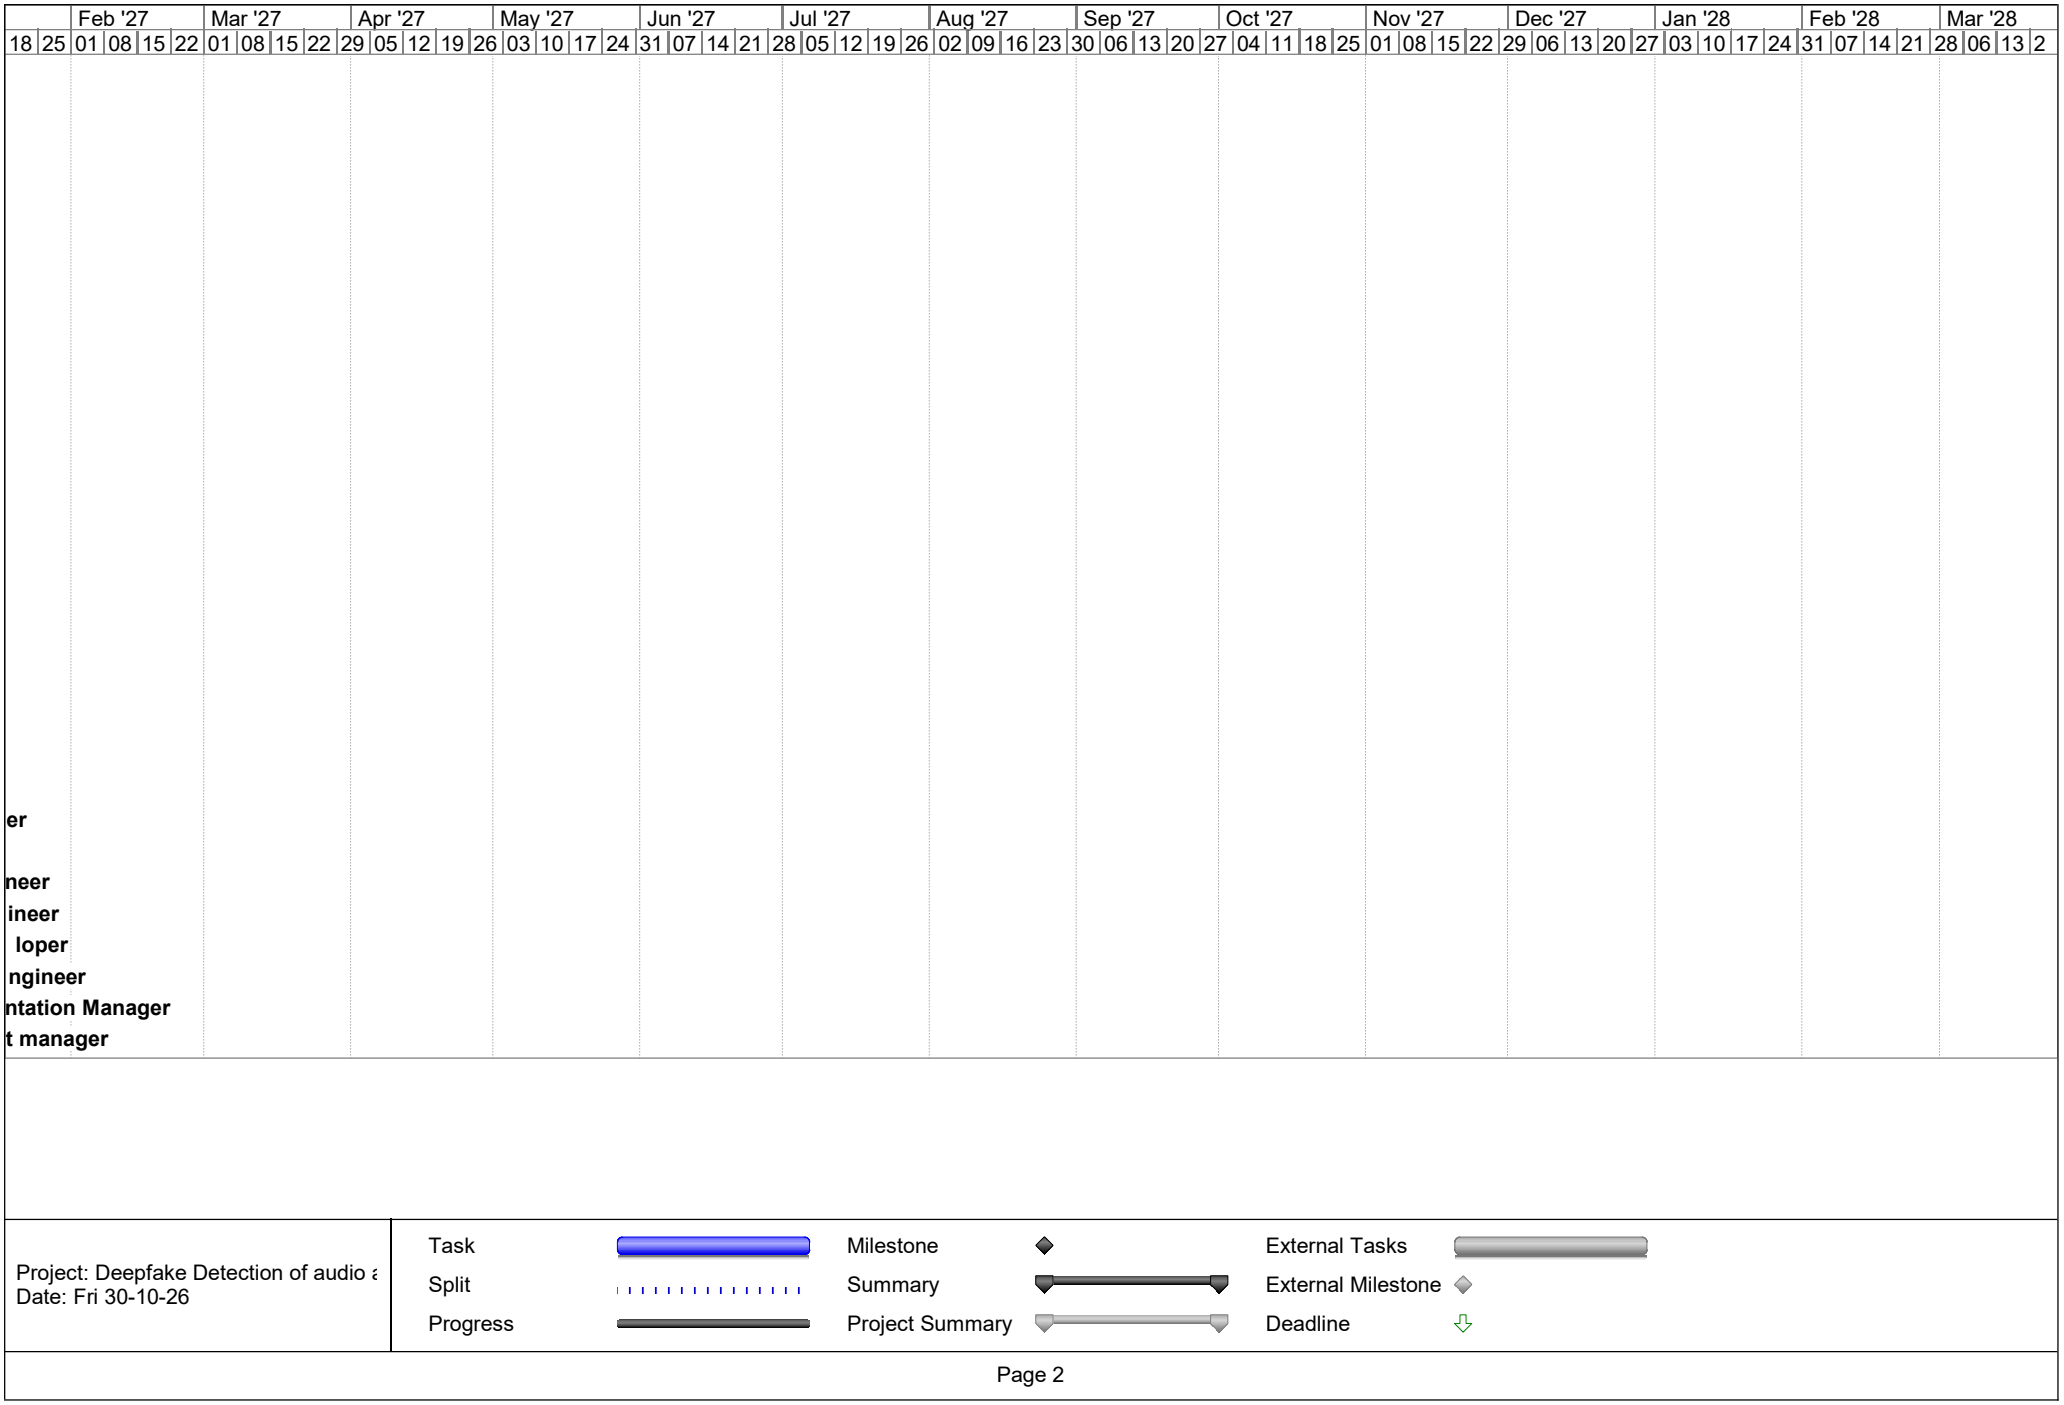

Project: Deepfake Detection of audio a
Date: Fri 30-10-26

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline


Feb '27
Mar '27
Apr '27
May '27
Jun '27
Jul '27
Aug '27
Sep '27
Oct '27
Nov '27
Dec '27
Jan '28
Feb '28
Mar '28
18 25 01 08 15 22 01 08 15 22 29 05 12 19 26 03 10 17 24 31 07 14 21 28 05 12 19 26 02 09 16 23 30 06 13 20 27 04 11 18 25 01 08 15 22 29 06 13 20 27 03 10 17 24 31 07 14 21 28 06 13 2
er
neer
ineer
loper
ngineer
ntation Manager
t manager
Project: Deepfake Detection of audio a
Date: Fri 30-10-26
Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline
