**DEEPFAKE DETECTION OF A**

Start: 30-10-26 ID: 1
Finish: 29-12-26 Dur: 43 days?
Comp: 0%

Start: 30-10-26 ID: 2
Finish: 30-10-26 Dur: 1 day?
Res:

**REQUIREMENT AND DESIGN**


Start: 30-10-26 ID: 3
Finish: 10-11-26 Dur: 8 days
Comp: 0%


**Project Planning and require**

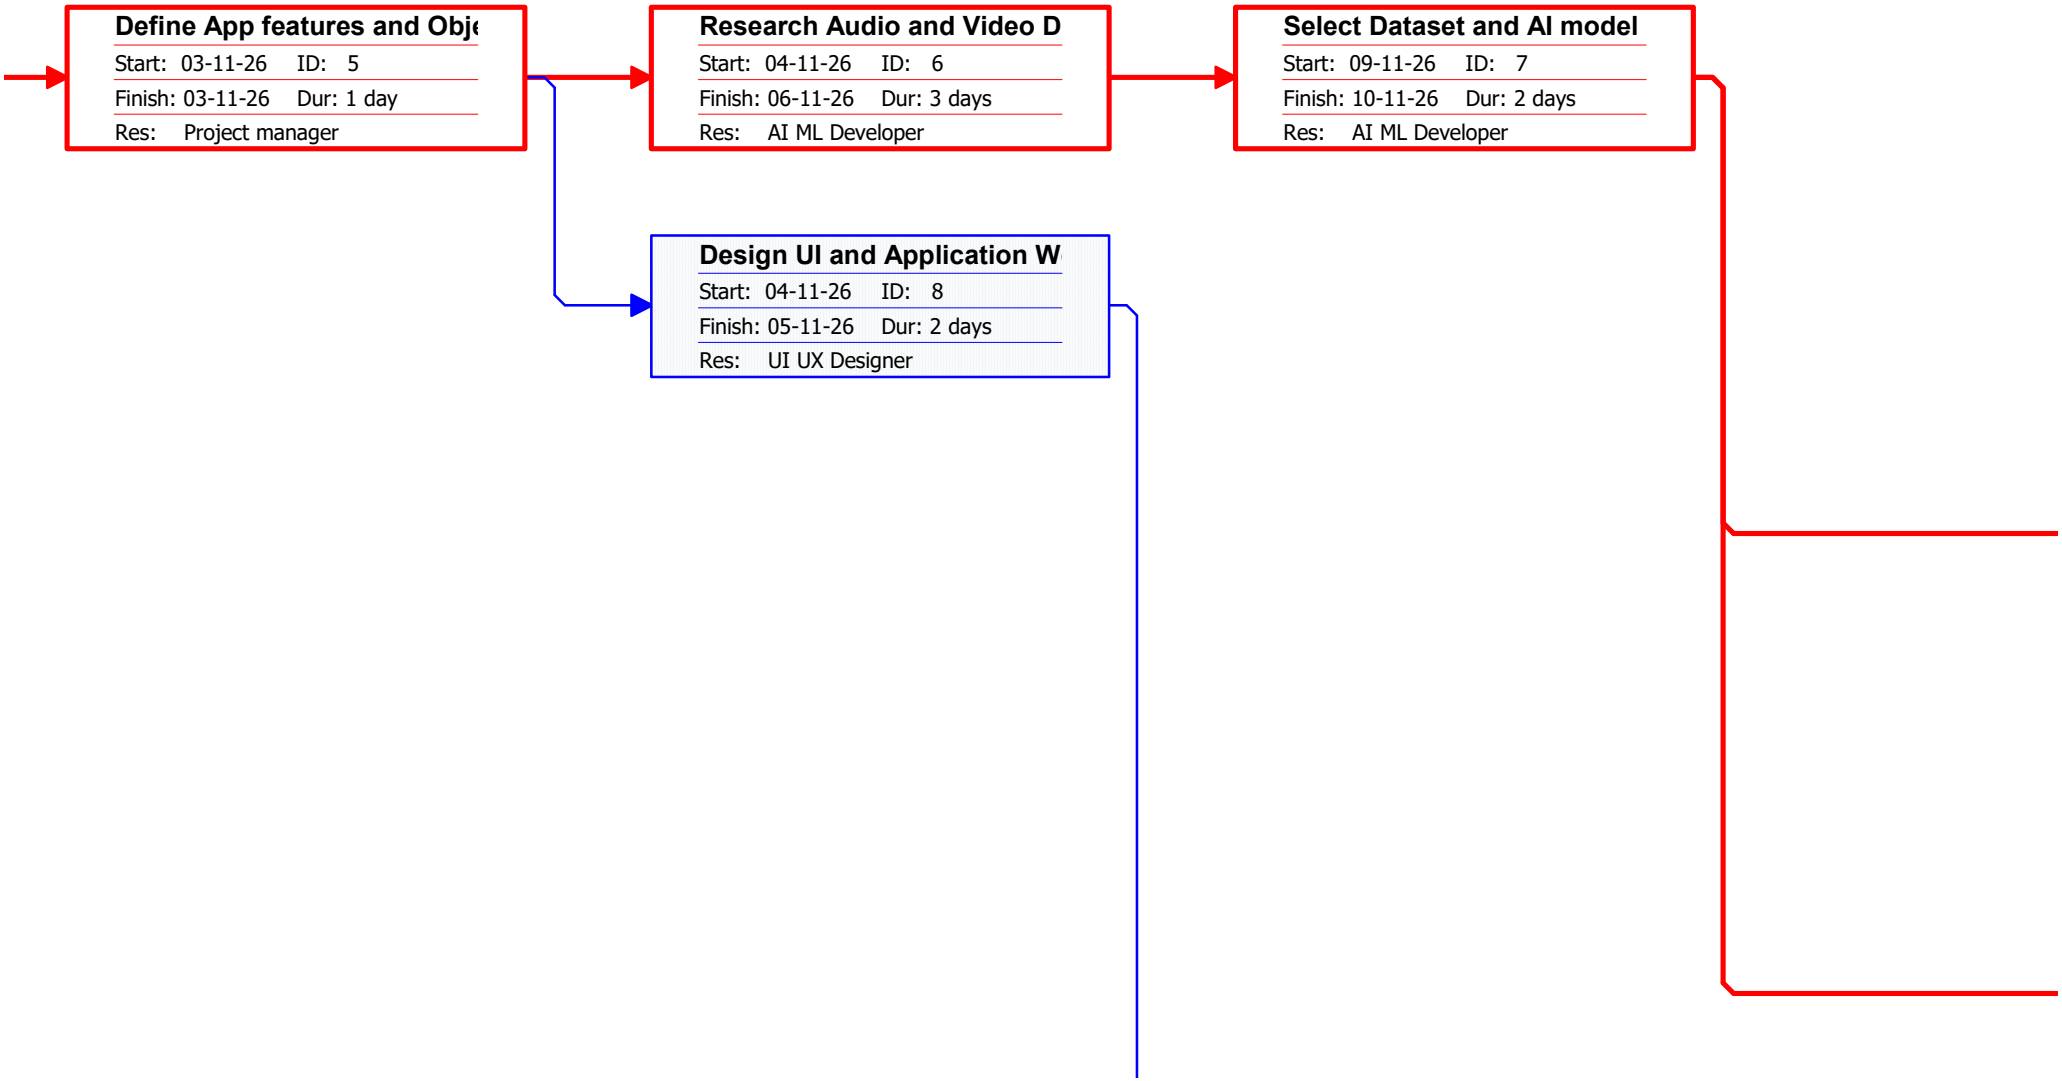
Start: 30-10-26 ID: 4
Finish: 02-11-26 Dur: 2 days
Res: Project manager


**DATSET AND AI MODEL**

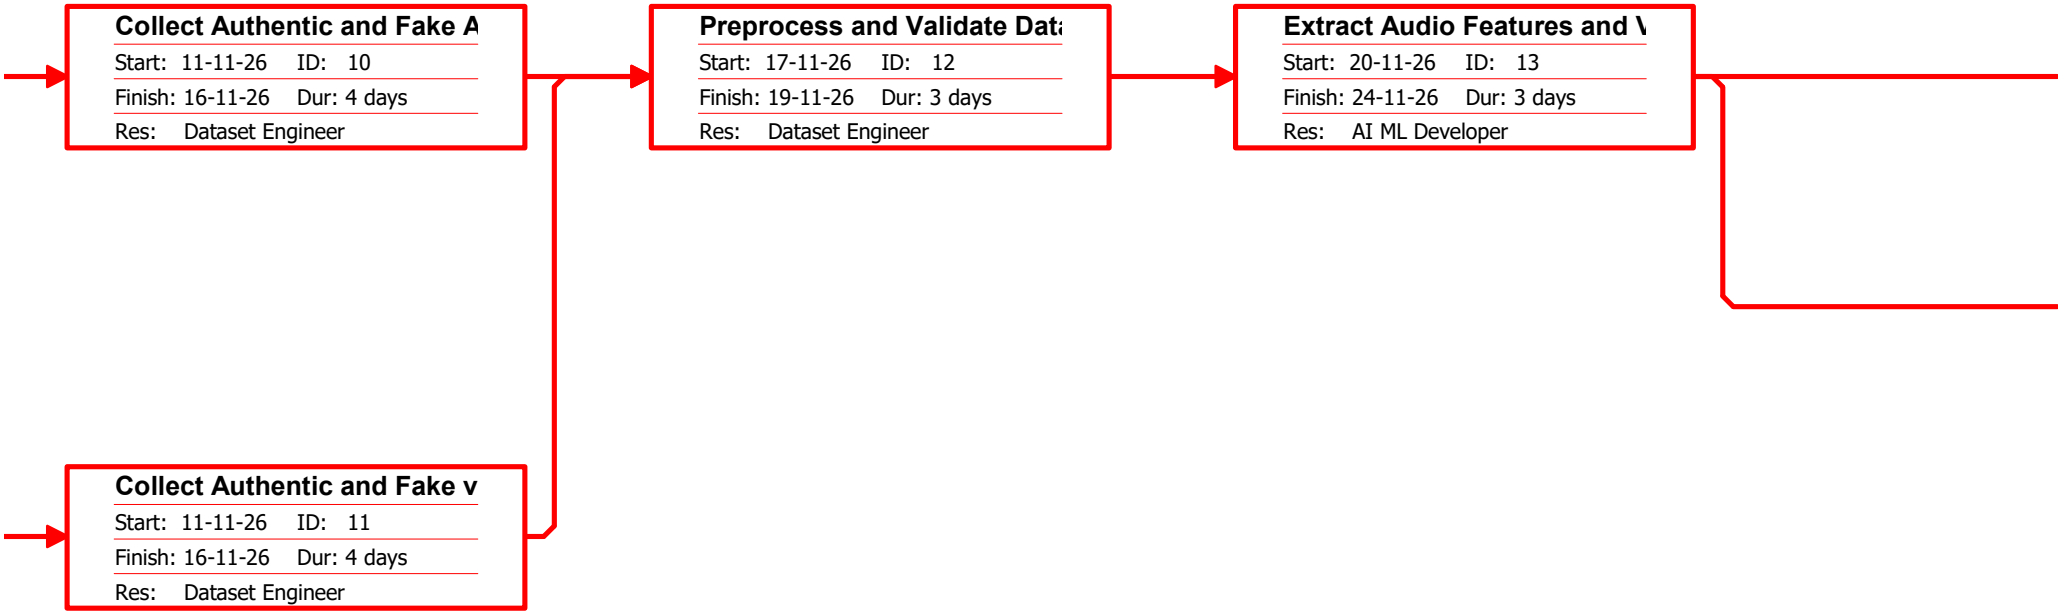
Start: 11-11-26 ID: 9
Finish: 02-12-26 Dur: 16 days
Comp: 0%

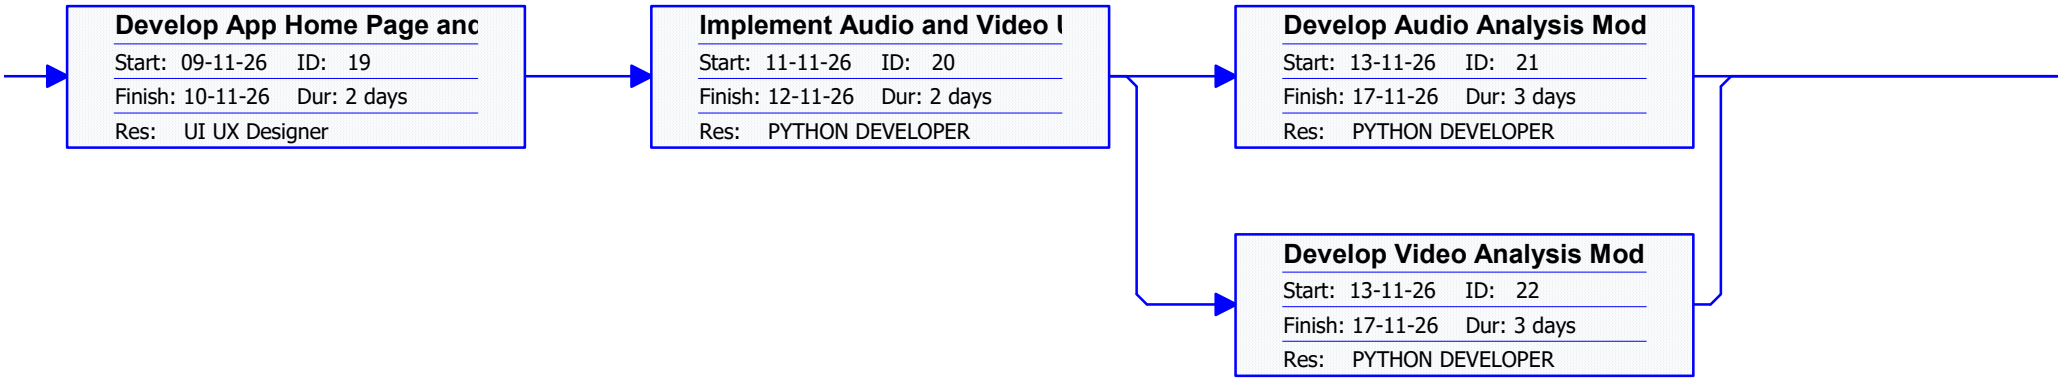

WEB APPLICATION DEVELO
Start: 06-11-26 ID: 17
Finish: 10-12-26 Dur: 25 days
Comp: 0%

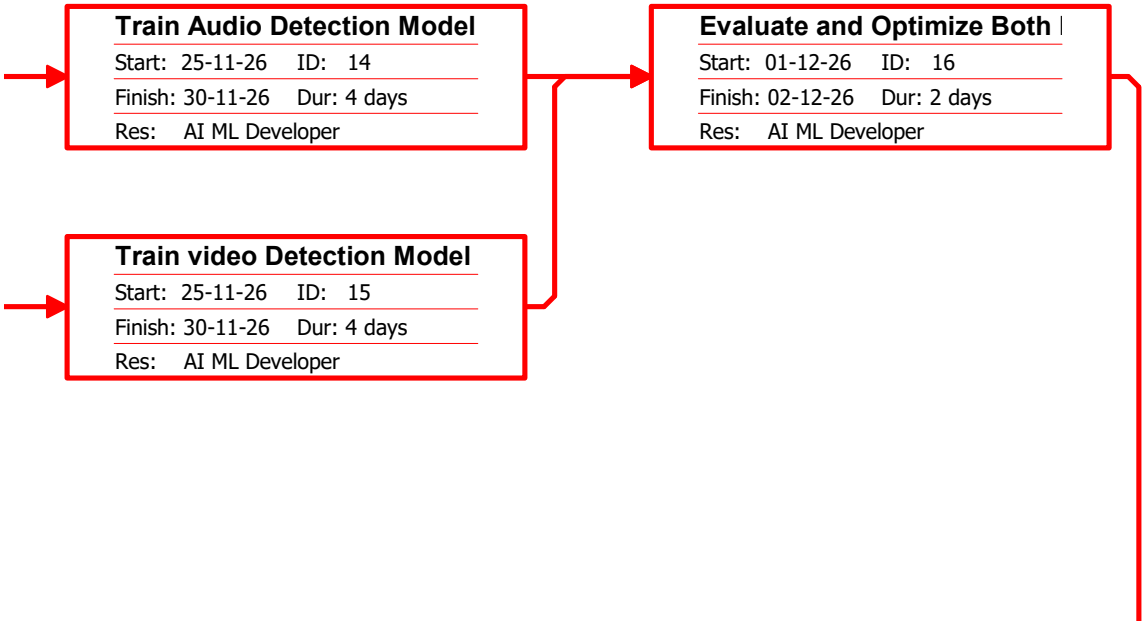

TESTING AND FINAL DELIVE
Start: 11-12-26 ID: 26
Finish: 29-12-26 Dur: 13 days
Comp: 0%



Define App features and Obje
Start: 03-11-26 ID: 5
Finish: 03-11-26 Dur: 1 day
Res: Project manager
Research Audio and Video D
Start: 04-11-26 ID: 6
Finish: 06-11-26 Dur: 3 days
Res: AI ML Developer
Select Dataset and AI model
Start: 09-11-26 ID: 7
Finish: 10-11-26 Dur: 2 days
Res: AI ML Developer
Design UI and Application W
Start: 04-11-26 ID: 8
Finish: 05-11-26 Dur: 2 days
Res: UI UX Designer

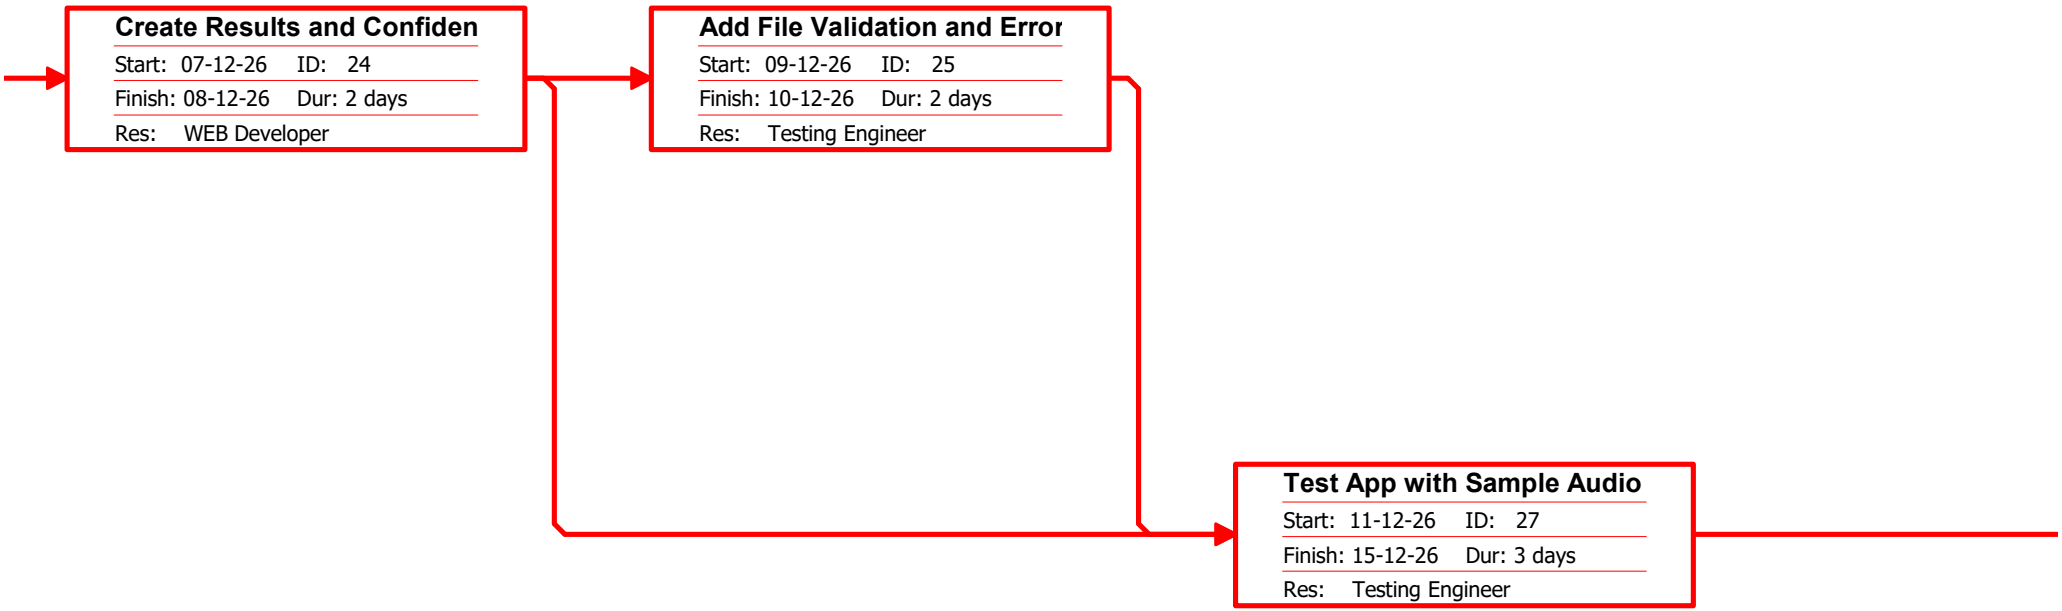

Set Up Python and Streamlit
Start: 06-11-26 ID: 18
Finish: 06-11-26 Dur: 1 day
Res: PYTHON DEVELOPER



Collect Authentic and Fake A
Start: 11-11-26 ID: 10
Finish: 16-11-26 Dur: 4 days
Res: Dataset Engineer
Preprocess and Validate Dat
Start: 17-11-26 ID: 12
Finish: 19-11-26 Dur: 3 days
Res: Dataset Engineer
Extract Audio Features and V
Start: 20-11-26 ID: 13
Finish: 24-11-26 Dur: 3 days
Res: AI ML Developer
Collect Authentic and Fake v
Start: 11-11-26 ID: 11
Finish: 16-11-26 Dur: 4 days
Res: Dataset Engineer



Develop App Home Page anc
Start: 09-11-26 ID: 19
Finish: 10-11-26 Dur: 2 days
Res: UI UX Designer
Implement Audio and Video I
Start: 11-11-26 ID: 20
Finish: 12-11-26 Dur: 2 days
Res: PYTHON DEVELOPER
Develop Audio Analysis Mod
Start: 13-11-26 ID: 21
Finish: 17-11-26 Dur: 3 days
Res: PYTHON DEVELOPER
Develop Video Analysis Mod
Start: 13-11-26 ID: 22
Finish: 17-11-26 Dur: 3 days
Res: PYTHON DEVELOPER


Train Audio Detection Model
Start: 25-11-26 ID: 14
Finish: 30-11-26 Dur: 4 days
Res: AI ML Developer
Train video Detection Model
Start: 25-11-26 ID: 15
Finish: 30-11-26 Dur: 4 days
Res: AI ML Developer
Evaluate and Optimize Both
Start: 01-12-26 ID: 16
Finish: 02-12-26 Dur: 2 days
Res: AI ML Developer


Integrate AI Models with App
Start: 03-12-26 ID: 23
Finish: 04-12-26 Dur: 2 days
Res: AI ML Developer


Create Results and Confiden
Start: 07-12-26 ID: 24
Finish: 08-12-26 Dur: 2 days
Res: WEB Developer
Add File Validation and Error
Start: 09-12-26 ID: 25
Finish: 10-12-26 Dur: 2 days
Res: Testing Engineer
Test App with Sample Audio
Start: 11-12-26 ID: 27
Finish: 15-12-26 Dur: 3 days
Res: Testing Engineer


Measure Model Performance
Start: 16-12-26 ID: 28
Finish: 17-12-26 Dur: 2 days
Res: Testing Engineer
Improve UI and Fix Identified
Start: 18-12-26 ID: 29
Finish: 22-12-26 Dur: 3 days
Res: WEB Developer
Deploy and Demonstrate the
Start: 23-12-26 ID: 30
Finish: 24-12-26 Dur: 2 days
Res: Deploy Engineer


Prepare Final Report and Pre
Start: 25-12-26 ID: 31
Finish: 28-12-26 Dur: 2 days
Res: ocumentation Manager
Final Review and Project Sub
Start: 29-12-26 ID: 32
Finish: 29-12-26 Dur: 1 day
Res: Project manager

Project: Deepfake Detection of audio a
Date: Fri 30-10-26

